

Battlefield Boulevard Continuous Right Turn Lane - Volvo to Walmart Way

UPC # 119232

OVERVIEW

Description: Convert the existing right-turn lane on Battlefield Boulevard at Coastal Way to a through-lane. Additionally, a new right-turn lane will be added at Coastal Way.

Street (Route): Battlefield Boulevard Northbound

From: Coastal Way

To: 270' North of Coastal Way

Length (mi): 0.27

Jurisdiction/Agency: Chesapeake

System: Urban

Scope: Reconstruction w/ Added Capacity

Oversight: Non-Federal Oversight

Administered By: Locality


Regionally Significant: No

CMAQ: No

RSTP: No

TAP: No

CRP: No

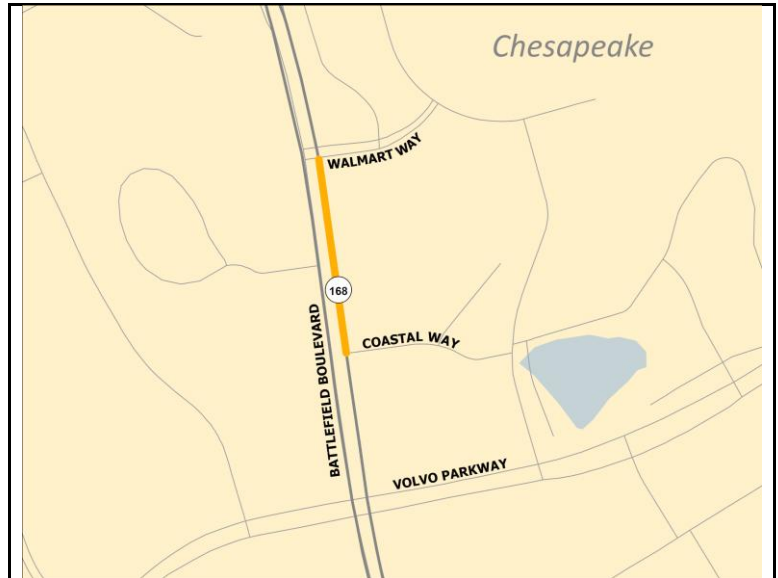

HRTPO Notes

Revised 7/28/2025: Administrative Modification to revise the description, cost estimate, schedule, allocations, and obligations. Revise cost estimate to be \$2,836,382. Update allocations as follows: add FY 2025 DGP-Sup-State allocation of \$700,000; remove FY 2026 STF allocation of \$1,400,000; add FY 2026 DGP-State allocation of \$1,400,000; add FY 2027 DGP-State allocation of \$736,382; remove FY 2027 STF allocation of \$1,436,382. Update the obligations as follows: remove FY 2025 PE Phase AC obligation of \$328,878; add FY 2025 PE Phase Other obligation of \$328,378; add FY 2025 RW Phase Other obligation of \$1,727,157; add FY 2026 CN Phase Phase Other obligation of \$780,848.

SCHEDULE

	Start	End	Status
Preliminary Engineering	11/22/2024	8/5/2025	Complete
Right of Way	8/5/2025	9/10/2026	Underway
Construction	9/10/2026	8/30/2027	FFY 2026

COSTS AND EXPENDITURES

	Cost Estimates	Total Expenditures	Percent Expended
Preliminary Engineering	\$328,378	\$1,096	0%
Right of Way	\$1,727,157	\$0	0%
Construction	\$780,847	\$0	0%
TOTAL	\$2,836,382	\$1,096	0%

Recent Expenditures

Latest Quarter	Previous 3 Quarters		
	3	2	1
	-	-	-
	-	-	-
	-	-	-

Battlefield Boulevard Continuous Right Turn Lane - Volvo to Walmart Way

UPC # 119232

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>TOTAL</i>
DGP-State	\$0	\$0	\$0	\$1,400,000	\$736,382	\$2,136,382
DGP-Sup-State	\$0	\$0	\$700,000	\$0	\$0	\$700,000
TOTAL	\$0	\$0	\$700,000	\$1,400,000	\$736,382	\$2,836,382

SCHEDULED OBLIGATIONS

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>Match</i>
PE	Other			\$328,378			
	Subtotal			\$328,378			
RW	Other			\$1,727,157			
	Subtotal			\$1,727,157			
CN	Other				\$780,848		
	Subtotal				\$780,848		
TOTAL				\$2,055,535	\$780,848		

Source of Project Data: Virginia Department of Transportation.
