

Military Highway Widening - Phase I (Project in Financial Closeout)

UPC # 84243

OVERVIEW

Description: Widen Military Hwy from 4 to 6 lanes from 0.3 mi north of Northampton Blvd (Rte 13) to the I-64 ramp to Robin Hood Rd.

Street (Route): Military Highway (165)

From: 0.3 miles north of Northampton Boulevard (Route 13)

To: I-64 Ramp to Robin Hood Road

Length (mi): 0.5

Jurisdiction/Agency: Norfolk

System: Urban

Scope: Reconstruction w/ Added Capacity


Oversight: Non-Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: Yes

CMAQ: No

RSTP: Yes

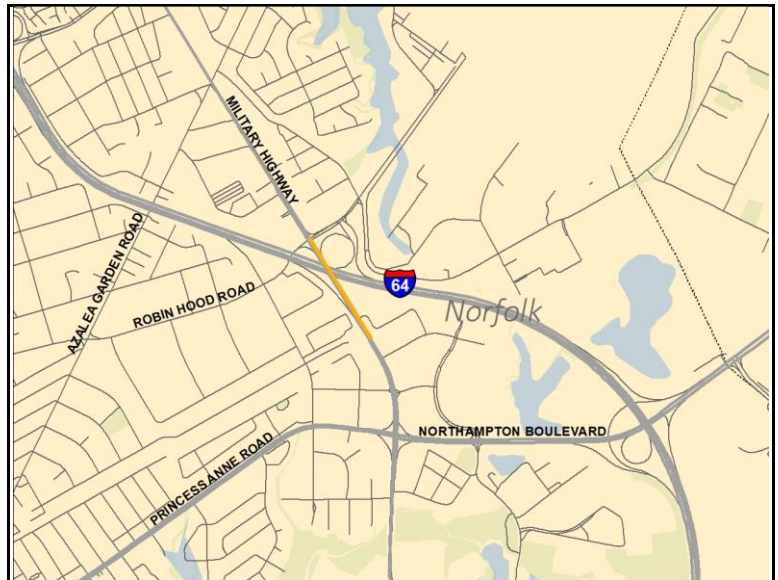

HRTPO Notes

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	N/A	N/A	N/A
<i>Right of Way</i>	12/19/2008	4/17/2015	Complete
<i>Construction</i>	4/17/2015	11/15/2018	Complete

COSTS AND EXPENDITURES

	Recent Expenditures			Previous 3 Quarters			
	Cost Estimates	Total Expenditures	Percent Expended	Latest Quarter	3	2	1
Preliminary Engineering	\$0	\$0	-	\$0	-	-	-
Right of Way	\$987,273	\$987,273	100%	\$0	-	-	-
Construction	\$18,092,014	\$18,092,014	100%	\$0	-	-	-
TOTAL	\$19,079,287	\$19,079,287	100%				

Military Highway Widening - Phase I (Project in Financial Closeout)

UPC # 84243

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>TOTAL</i>
STP	\$3,513,517	\$0	\$0	\$0	\$0	\$3,513,517
STM	\$1,422,365	\$0	\$0	\$0	\$0	\$1,422,365
STF	\$3,338,798	\$0	\$0	\$0	\$0	\$3,338,798
RSTP	\$8,689,461	\$0	\$0	\$0	\$0	\$8,689,461
MIX	\$3,910,036	\$0	\$0	\$0	\$0	\$3,910,036
LOM	\$298,095	\$0	\$0	\$0	\$0	\$298,095
GARV	\$4,267,199	\$0	\$0	\$0	\$0	\$4,267,199
EB/MG	\$28,424	\$0	\$0	\$0	\$0	\$28,424
BOM	\$798,357	\$0	\$0	\$0	\$0	\$798,357
TOTAL	\$26,266,252	\$0	\$0	\$0	\$0	\$26,266,252

SCHEDULED OBLIGATIONS

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>Match</i>
CN	NHS/NHPP	\$1,321,344	\$232,737				
CN	AC-Conv			\$244,550	\$256,924	\$269,912	
CN	AC		\$1,888,514				
Subtotal		\$1,321,344	\$2,121,251	\$244,550	\$256,924	\$269,912	
TOTAL		\$1,321,344	\$2,121,251	\$244,550	\$256,924	\$269,912	

Source of Project Data: Virginia Department of Transportation.
