

Jefferson Avenue and Yorktown Road Intersection Improvements
UPC # 111091

OVERVIEW

Description: Construct a second eastbound lane through the intersection.

Street (Route): Yorktown Road

From: 0.25 miles south of Jefferson Avenue

To: 0.25 miles north of Jefferson Avenue

Length (mi): 0.5

Jurisdiction/Agency: Newport News

System: Urban

Scope: Reconstruction w/ Added Capacity


Oversight: Non-Federal Oversight

Administered By: Locality

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

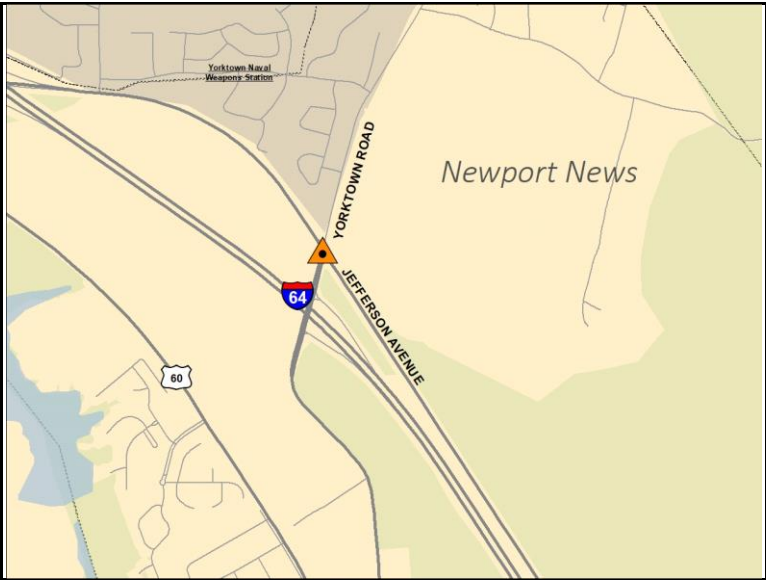

HRTPO Notes

SCHEDULE

	Start	End	Status
Preliminary Engineering	12/2/2021	3/16/2023	Complete
Right of Way	3/16/2023	6/12/2024	Underway
Construction	6/12/2024	11/13/2025	FFY 2024

COSTS AND EXPENDITURES

	Cost Estimates	Total Expenditures	Percent Expended	Recent Expenditures			
				Latest Quarter	Previous 3 Quarters		
					3	2	1
Preliminary Engineering	\$395,000	\$3,700	1%	\$3,700	-	-	-
Right of Way	\$508,000	\$0	0%	\$0	-	-	-
Construction	\$1,557,000	\$0	0%	\$0	-	-	-
TOTAL	\$2,460,000	\$3,700	0%				

Jefferson Avenue and Yorktown Road Intersection Improvements
UPC # 111091

ALLOCATIONS

Fund Source(s)	Previous	FY 2024	FY 2025	FY 2026	FY 2027	TOTAL
STP	\$1,954,390	\$0	\$0	\$0	\$0	\$1,954,390
STF	\$505,610	\$0	\$0	\$0	\$0	\$505,610
TOTAL	\$2,460,000	\$0	\$0	\$0	\$0	\$2,460,000

SCHEDULED OBLIGATIONS

Phase	Fund Source	Previous	FY 2024	FY 2025	FY 2026	FY 2027	Match
RW	STP/STBG		\$508,000				
	Subtotal		\$508,000				
CN	STP/STBG		\$1,051,390				
CN	AC		\$505,610				
	Subtotal		\$1,557,000				
	TOTAL		\$2,065,000				

Source of Project Data: Virginia Department of Transportation.
