

Wythe Creek Road Traffic Signal Upgrade (Project in Financial Closeout)

UPC # 102999

OVERVIEW

Description: Upgrade the traffic signals on Wythe Creek Road to connect to the City of Hampton traffic signal network.

Street (Route): Wythe Creek Road (172)

From: Hampton City Line

To: Yorktown Road

Length (mi): N/A

Jurisdiction/Agency: Poquoson

System: Urban

Scope: Traffic Management/Engineering

Oversight: Non-Federal Oversight

Administered By: Locality


Regionally Significant: No

CMAQ: Yes

RSTP: No

TAP: No

CRP: No

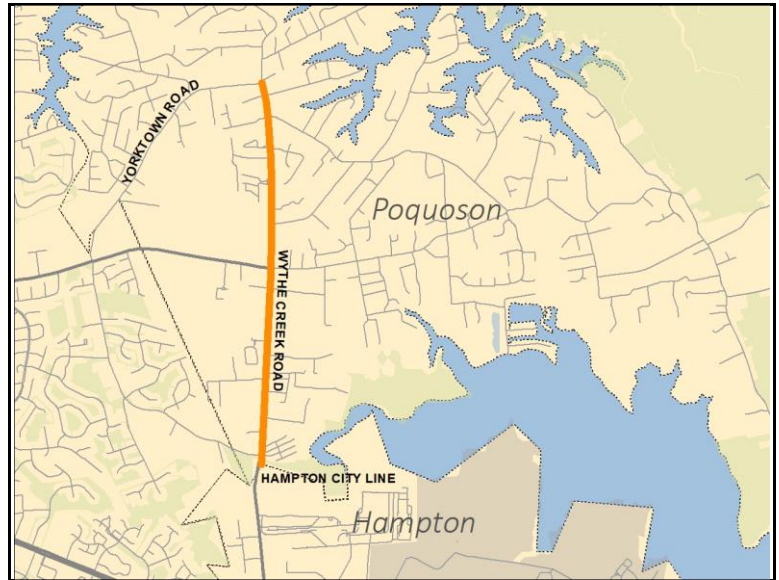

HRTPO Notes

Revised 2/4/2025: Administrative Modification to transfer FY 2018 CMAQ allocation of \$43,176, plus \$10,794 CMAQ match, to the HRTPO CMAQ Reserve Account.

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	4/2/2018	8/28/2020	Complete
<i>Right of Way</i>	N/A	N/A	N/A
<i>Construction</i>	8/28/2020	8/12/2021	Complete

COSTS AND EXPENDITURES

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>			
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
					<i>3</i>	<i>2</i>	<i>1</i>
<i>Preliminary Engineering</i>	\$95,621	\$95,621	100%	\$69	\$33	\$92	\$1,193
<i>Right of Way</i>	\$0	\$0	-	\$0	-	-	-
<i>Construction</i>	\$122,909	\$128,408	104%	\$125,796	\$1,738	\$756	\$118
TOTAL	\$218,530	\$224,029	103%				

Wythe Creek Road Traffic Signal Upgrade (Project in Financial Closeout)
UPC # 102999

ALLOCATIONS

Fund Source(s)	Previous	FY 2024	FY 2025	FY 2026	FY 2027	TOTAL
CMAQ Match	\$44,806	\$0	\$0	\$0	\$0	\$44,806
CMAQ	\$179,224	\$0	\$0	\$0	\$0	\$179,224
TOTAL	\$224,030	\$0	\$0	\$0	\$0	\$224,030

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
