

**I-64 Peninsula Widening - Segment 3**  
**UPC # 106689**

**OVERVIEW**

**Description:** Extend the 3 lane section of I-64 from Rt 199 East of Williamsburg (Exit 242) to Rt 199 West of Williamsburg (Exit 234). Work to include one additional EB and WB 12' wide travel lane and 12' wide shoulder lane within the existing median space.

**Street (Route):** I-64 (64)

**Length (mi):** 8.23

**Jurisdiction/Agency:** Hampton Roads

**System:** Interstate

**Scope:** Reconstruction with added capacity


**Oversight:** Federal Oversight

**Administered By:** VDOT

**Regionally Significant for Air Quality:** Yes

**CMAQ:** No

**RSTP:** No

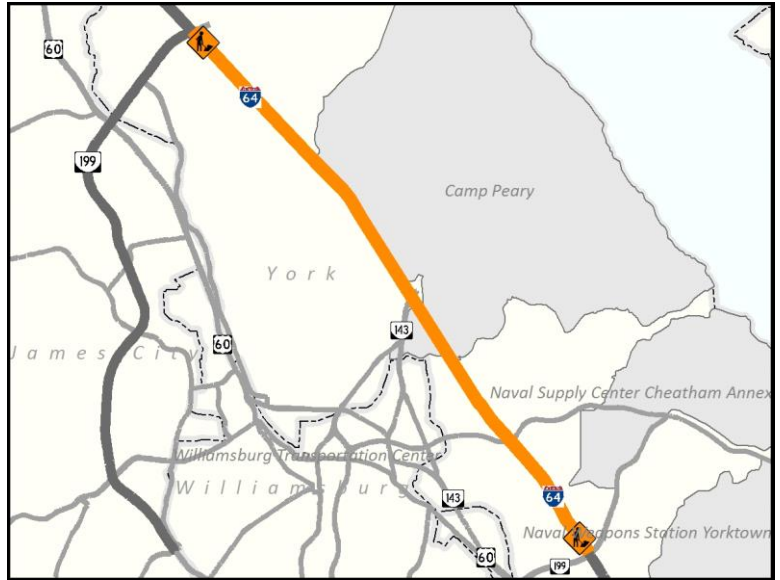

**HRTPO Notes**

**SCHEDULE**

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	3/1/2016	6/21/2017	Complete
<i>Right of Way</i>	6/21/2017	6/21/2017	Complete
<i>Construction</i>	6/21/2017	9/24/2021	Underway

**COSTS AND EXPENDITURES**

**Recent Expenditures**

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
					<i>3</i>	<i>2</i>	<i>1</i>
<i>Preliminary Engineering</i>	\$10,000,000	\$5,291,519	53%	\$0	-	-	-
<i>Right of Way</i>	\$0	\$0	-	\$0	-	-	-
<i>Construction</i>	\$112,893,996	\$12,092,634	11%	\$0	-	-	-
<b>TOTAL</b>	<b>\$122,893,996</b>	<b>\$17,384,153</b>	<b>14%</b>				

**ALLOCATIONS**

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>TOTAL</i>
HRTAC	\$116,474,798	\$6,419,198	\$0	\$0	\$0	\$122,893,996
<b>TOTAL</b>	<b>\$116,474,798</b>	<b>\$6,419,198</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$122,893,996</b>

## SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
