

I-264 - Interchange Improvements I-64 West to 264 East w/57048

UPC # 108042

OVERVIEW

Description: This project is for tracking UPC 57048 project charges associated with HRTAC funding.

Street (Route): I-264

Length (mi): N/A

Jurisdiction/Agency: Norfolk

System: Interstate

Scope: Reconstruction


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

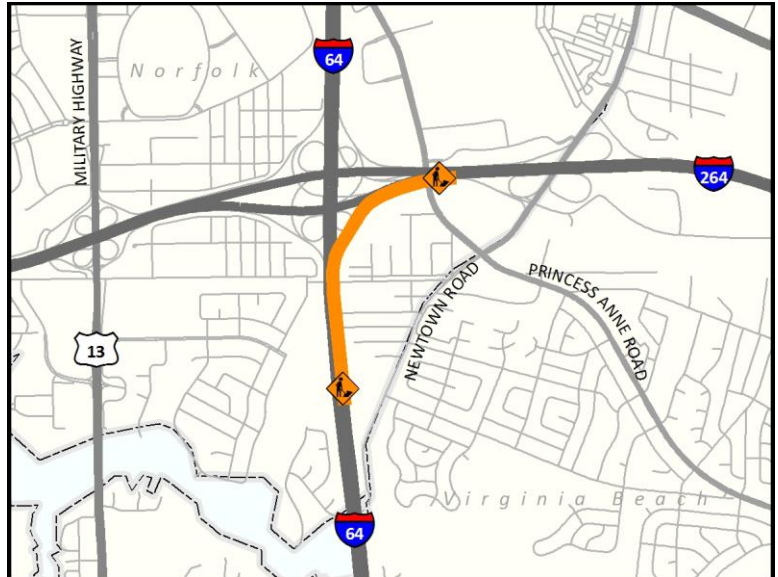

HRTPO Notes

SCHEDULE

	Start	End	Status
Preliminary Engineering	2/28/2001	4/30/2015	Complete
Right of Way	4/30/2015	4/12/2016	Complete
Construction	4/12/2016	N/A	N/A

COSTS AND EXPENDITURES

	Cost Estimates	Total Expenditures	Percent Expended	Recent Expenditures			
				Latest Quarter	Previous 3 Quarters		
				3	2	1	
Preliminary Engineering	\$3,500,000	\$3,500,000	100%	\$0	-	-	-
Right of Way	\$11,571,063	\$20,431,775	177%	\$0	-	-	-
Construction	\$137,023,653	\$115,465,431	84%	\$0	-	-	-
TOTAL	\$152,094,716	\$139,397,206	92%				

ALLOCATIONS

Fund Source(s)	Previous	FY 2021	FY 2022	FY 2023	FY 2024	TOTAL
HRTAC	\$152,094,716	\$0	\$0	\$0	\$0	\$152,094,716
TOTAL	\$152,094,716	\$0	\$0	\$0	\$0	\$152,094,716

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
