

# Brambleton Avenue and Park Avenue Intersection Improvements

## UPC # 111019

### OVERVIEW

**Description:** Add a northbound right turn lane on Park Avenue

**Street (Route):** Park Avenue

**Length (mi):** 0.05

**Jurisdiction/Agency:** Norfolk

**System:** Urgan

**Scope:** Reconstruction w/Added Capacity


**Oversight:** Federal Oversight

**Administered By:** Locality

**Regionally Significant for Air Quality:** Yes

**CMAQ:** No

**RSTP:** No

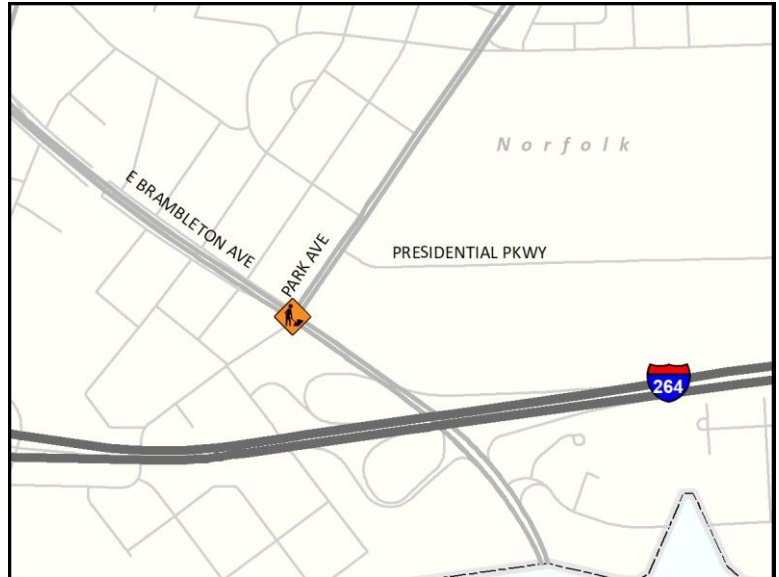

### HRTPO Notes

Revised 3/9/2021: Administrative Modification to revise the obligations as part of the FY 21-24 rollover process. Update obligations as follows: add FY Previous PE Phase AC-Other obligation of \$93,000; remove FY 2022 RW Phase AC obligation of \$67,000; remove FY 2023 CN Phase AC obligation of \$434,000.

### SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	8/25/2020	2/7/2022	Underway
<i>Right of Way</i>	2/7/2022	3/7/2023	FFY 2022
<i>Construction</i>	3/7/2023	2/12/2025	FFY 2023

### COSTS AND EXPENDITURES

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>			
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
				<i>3</i>	<i>2</i>	<i>1</i>	
<i>Preliminary Engineering</i>	\$93,000	\$0	0%	\$0	-	-	-
<i>Right of Way</i>	\$67,000	\$0	0%	\$0	-	-	-
<i>Construction</i>	\$434,000	\$0	0%	\$0	-	-	-
<b>TOTAL</b>	<b>\$594,000</b>	<b>\$0</b>	<b>0%</b>				

### ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>TOTAL</i>
STF	\$0	\$93,000	\$67,000	\$434,000	\$0	\$594,000
<b>TOTAL</b>	<b>\$0</b>	<b>\$93,000</b>	<b>\$67,000</b>	<b>\$434,000</b>	<b>\$0</b>	<b>\$594,000</b>

**SCHEDULED OBLIGATIONS**

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>Match</i>
PE	AC-Other	\$93,000					
	<b>Subtotal</b>	<b>\$93,000</b>					
<b>TOTAL</b>		<b>\$93,000</b>					

Source of Project Data: Virginia Department of Transportation.
