

I-264 West Off-Ramp Improvements at Ballentine Boulevard

UPC # 111788

OVERVIEW

Description: Addition of dual right turn lane on the I-264 West off-ramp at Ballentine Boulevard

Street (Route): N/A

Length (mi): 0.09

Jurisdiction/Agency: Norfolk

System: Interstate

Scope: Traffic Management/Engineering


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

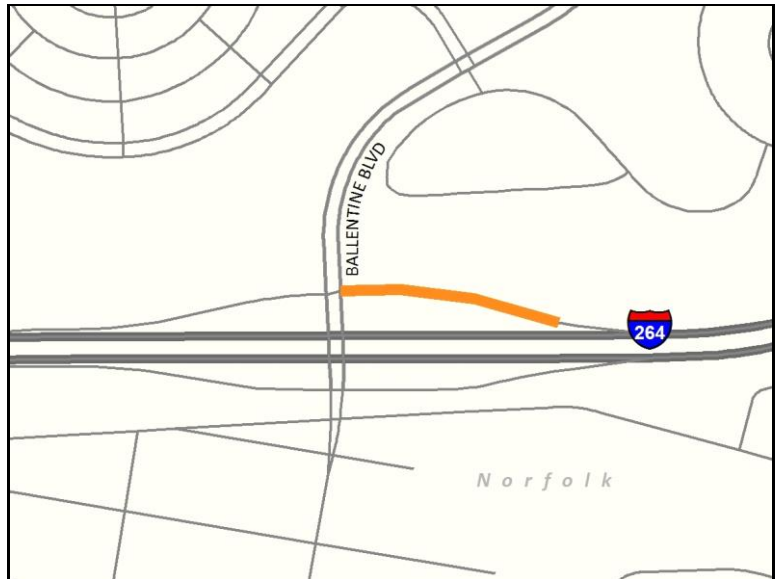

HRTPO Notes

Revised 3/9/2021: Administrative Modification to update the schedule and obligations as part of the FY 21-24 rollover process. Update obligations as follows: add FY Previous PE Phase STP obligation of \$200,000; remove FY 2021 PE Phase STP/STBG obligation of \$200,000; remove FY 2022 RW Phase STP/STBG obligation of \$180,000; remove FY 2024 CN Phase STP/STBG obligation of \$1,130,000; remove FY 2024 CN Phase AC obligation of \$200,000. Revised 5/4/2021: Administrative Modification to revise the schedule and obligations. Update obligations as follows: add FY 2021 PE Phase STP/STBG obligation of \$20,000.

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	11/25/2019	4/24/2023	Underway
<i>Right of Way</i>	4/24/2023	7/9/2024	FFY 2023
<i>Construction</i>	7/9/2024	8/4/2025	FFY 2024

COSTS AND EXPENDITURES

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>		
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>	
				<i>3</i>	<i>2</i>	<i>1</i>
<i>Preliminary Engineering</i>	\$200,000	\$0	0%	\$0	-	-
<i>Right of Way</i>	\$180,000	\$0	0%	\$0	-	-
<i>Construction</i>	\$1,330,000	\$0	0%	\$0	-	-
TOTAL	\$1,710,000	\$0	0%			

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>TOTAL</i>
STP	\$0	\$180,000	\$820,000	\$510,000	\$0	\$1,510,000
STF	\$200,000	\$0	\$0	\$0	\$0	\$200,000
TOTAL	\$200,000	\$180,000	\$820,000	\$510,000	\$0	\$1,710,000

SCHEDULED OBLIGATIONS

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>Match</i>
PE	STP/STBG	\$200,000	\$20,000				
	Subtotal	\$200,000	\$20,000				
	TOTAL	\$200,000	\$20,000				

Source of Project Data: Virginia Department of Transportation.
