

Route 171 (Victory Blvd) Right Turn Lane Extension in York County
UPC # 113633

OVERVIEW

Description: Extend the westbound Victory Blvd right turn lane at Kiln Creek

Street (Route): Victory Boulevard

Length (mi): 0.14

Jurisdiction/Agency: York County

System: Primary

Scope: Safety


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

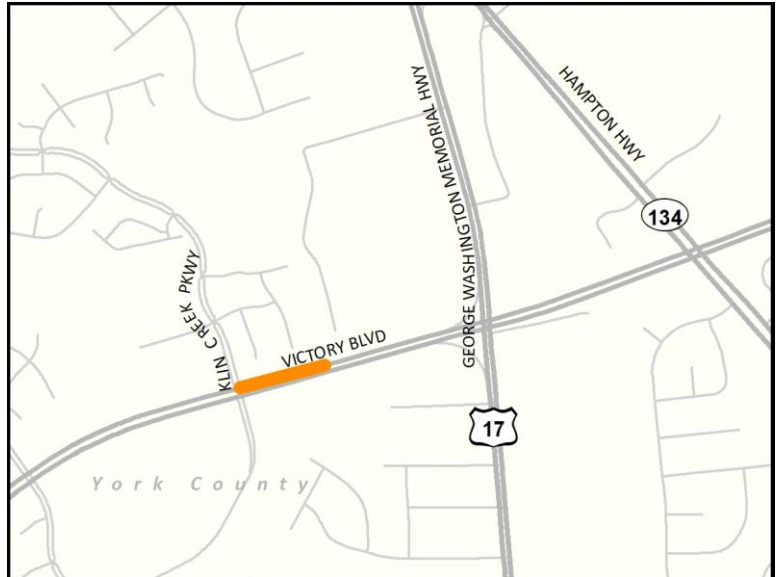

HRTPO Notes

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	10/31/2022	12/10/2024	FFY 2023
<i>Right of Way</i>	N/A	N/A	N/A
<i>Construction</i>	12/10/2024	10/14/2025	FFY 2025

COSTS AND EXPENDITURES

Recent Expenditures

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Previous 3 Quarters</i>			
				<i>Latest Quarter</i>	<i>3</i>	<i>2</i>	<i>1</i>
<i>Preliminary Engineering</i>	\$67,665	\$0	0%	\$0	-	-	-
<i>Right of Way</i>	\$0	\$0	-	\$0	-	-	-
<i>Construction</i>	\$347,118	\$0	0%	\$0	-	-	-
TOTAL	\$414,783	\$0	0%				

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>TOTAL</i>
SFTY	\$0	\$0	\$0	\$67,665	\$0	\$67,665
TOTAL	\$0	\$0	\$0	\$67,665	\$0	\$67,665

SCHEDULED OBLIGATIONS

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>Match</i>
PE	HSIP				\$67,665		
	Subtotal				\$67,665		
	TOTAL				\$67,665		

Source of Project Data: Virginia Department of Transportation.
