

Suffolk Seaboard Coastline Trail - Segment 1

UPC # 115525

OVERVIEW

Description: Segment 1 of the Suffolk Seaboard Coastline Trail, a 1.5 mile, 10-ft wide multi-use path, which is part of an 11 mile trail

Street (Route): N/A

Length (mi): 1.5

Jurisdiction/Agency: Suffolk

System: Urban

Scope: Facilities for Pedestrians and Bicycles


Oversight: Federal Oversight

Administered By: Locality

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

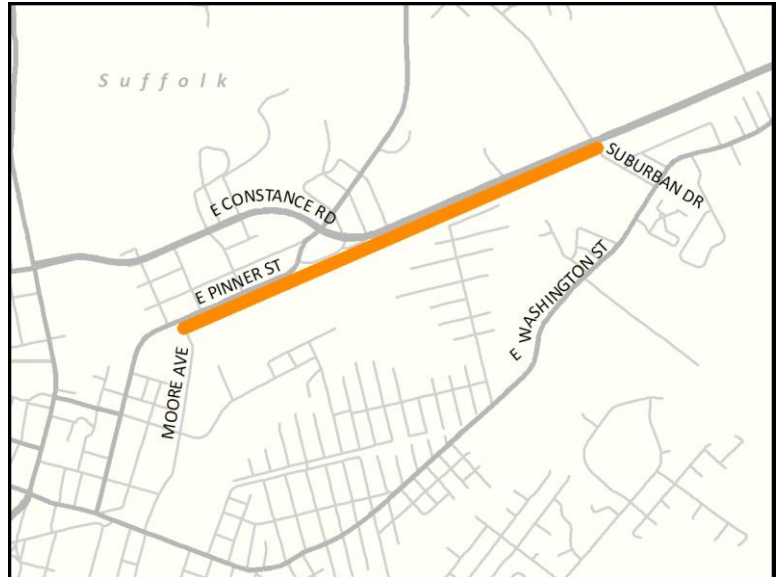

HRTPO Notes

SCHEDULE

	Start	End	Status
Preliminary Engineering	7/28/2023	3/4/2025	FFY 2023
Right of Way	3/4/2025	1/30/2026	FFY 2025
Construction	1/30/2026	6/11/2027	FFY 2026

COSTS AND EXPENDITURES

Recent Expenditures

	Cost Estimates	Total Expenditures	Percent Expended	Latest Quarter	Previous 3 Quarters		
					3	2	1
Preliminary Engineering	\$355,949	\$0	0%	\$0	-	-	-
Right of Way	\$77,875	\$0	0%	\$0	-	-	-
Construction	\$3,789,265	\$0	0%	\$0	-	-	-
TOTAL	\$4,223,089	\$0	0%				

ALLOCATIONS

Fund Source(s)	Previous	FY 2021	FY 2022	FY 2023	FY 2024	TOTAL
STF	\$0	\$0	\$0	\$0	\$2,000,000	\$2,000,000
TOTAL	\$0	\$0	\$0	\$0	\$2,000,000	\$2,000,000

SCHEDULED OBLIGATIONS

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>Match</i>
PE	AC				\$355,949		
	Subtotal				\$355,949		
	TOTAL				\$355,949		

Source of Project Data: Virginia Department of Transportation.
