

I-64 Express Lanes - Segment 4C - Phase 1 (PE Only) (Project in Financial Closeout)

UPC # 117841

OVERVIEW

Description: Widen EB and WB of I-64 from the eastern end of the LaSalle Avenue to approximately 2,000 feet east of the Settlers Landing Road overpass.

Street (Route): I-64

From: 0.14 miles east of LaSalle Avenue

To: 0.34 miles east of Settlers Landing Road

Length (mi): 2.5

Jurisdiction/Agency: Hampton

System: Interstate

Scope: Bridge Replacement w/ Added Capacity


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

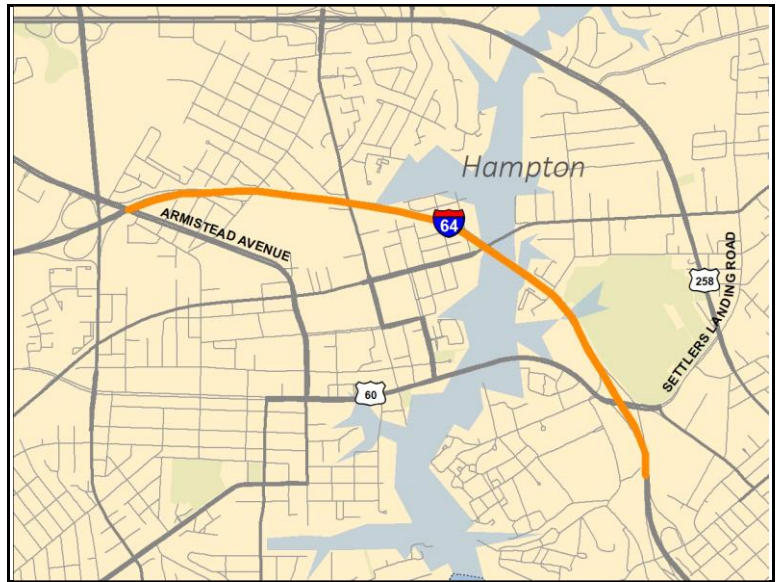

HRTPO Notes

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	9/22/2020	11/27/2023	Complete
<i>Right of Way</i>	N/A	N/A	N/A
<i>Construction</i>	N/A	N/A	N/A

COSTS AND EXPENDITURES

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>			
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
				<i>3</i>	<i>2</i>	<i>1</i>	
<i>Preliminary Engineering</i>	\$15,421,200	\$6,049,276	39%	\$3,185,650	\$801,244	\$1,316,632	\$562,494
<i>Right of Way</i>	\$0	\$0	-	\$0	-	-	-
<i>Construction</i>	\$0	\$0	-	\$0	-	-	-
TOTAL	\$15,421,200	\$6,049,276	39%				

I-64 Express Lanes - Segment 4C - Phase 1 (PE Only) (Project in Financial Closeout)

UPC # 117841

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>TOTAL</i>
LOC	\$15,421,200	\$0	\$0	\$0	\$0	\$15,421,200
TOTAL	\$15,421,200	\$0	\$0	\$0	\$0	\$15,421,200

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
