

# HRELN - Segment 4A/4B (Associated with UPC 117839)

UPC # 119824

## OVERVIEW

**Description:** Convert existing HOV lane into an HOT managed lane for the portion of the segment where these lanes are located - a portion of PE is being completed under UPC 117839.

**Street (Route):** I-64

**From:** 1.2 miles west of Denbigh Boulevard

**To:** 0.139 miles east of LaSalle Avenue

**Length (mi):** 13.39

**Jurisdiction/Agency:** Newport News

**System:** Interstate

**Scope:** Reconstruction w/ Added Capacity


**Oversight:** Federal Oversight

**Administered By:** VDOT

**Regionally Significant for Air Quality:** Yes

**CMAQ:** No

**RSTP:** No

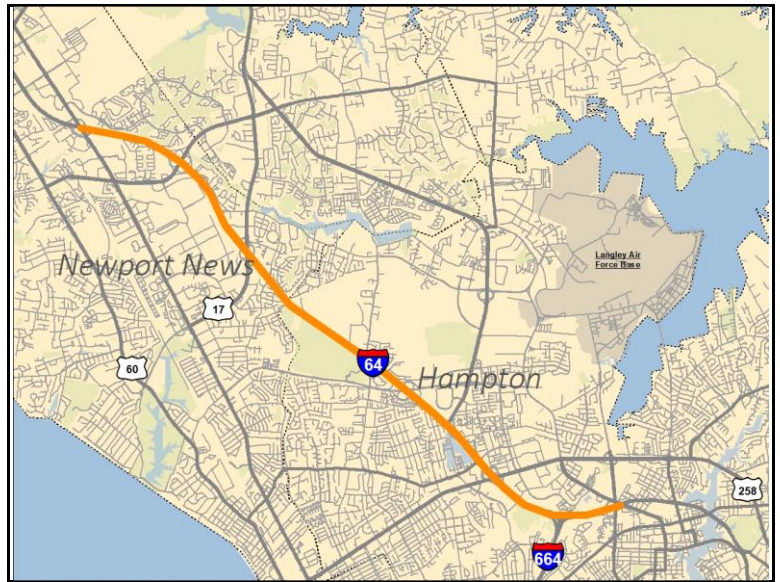

## HRTPO Notes

## SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	5/2/2022	12/16/2022	Complete
<i>Right of Way</i>	12/16/2022	5/14/2024	Underway
<i>Construction</i>	5/14/2024	12/30/2026	FFY 2024

## COSTS AND EXPENDITURES

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>			
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
				<i>3</i>	<i>2</i>	<i>1</i>	
<i>Preliminary Engineering</i>	\$10,052,520	\$1,509,832	15%		-	-	-
<i>Right of Way</i>	\$2,369,034	\$0	0%		-	-	-
<i>Construction</i>	\$137,884,376	\$0	0%		-	-	-
<b>TOTAL</b>	<b>\$150,305,930</b>	<b>\$1,509,832</b>	<b>1%</b>				

**HRELN - Segment 4A/4B (Associated with UPC 117839)**

**UPC # 119824**

**ALLOCATIONS**

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>TOTAL</i>
LOC	\$12,421,553	\$53,376,876	\$53,376,876	\$31,130,626	\$0	\$150,305,931
<b>TOTAL</b>	<b>\$12,421,553</b>	<b>\$53,376,876</b>	<b>\$53,376,876</b>	<b>\$31,130,626</b>	<b>\$0</b>	<b>\$150,305,931</b>

**SCHEDULED OBLIGATIONS**

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2024</i>	<i>FY 2025</i>	<i>FY 2026</i>	<i>FY 2027</i>	<i>Match</i>
RW	AC		\$2,369,034				
<b>Subtotal</b>			<b>\$2,369,034</b>				
CN	AC		\$137,884,376				
<b>Subtotal</b>			<b>\$137,884,376</b>				
<b>TOTAL</b>			<b>\$140,253,410</b>				

Source of Project Data: Virginia Department of Transportation.
