

Atkinson Boulevard Construction

UPC # 4483

OVERVIEW

Description: Construct a 4 lane roadway from Warwick Blvd (Rte 60) to Jefferson Ave (Rte 143)

Street (Route): Atkinson Boulevard

Length (mi): 1.2

Jurisdiction/Agency: Newport News

System: Urban

Scope: New Construction


Oversight: Non-Federal Oversight

Administered By: Locality

Regionally Significant for Air Quality: Yes

CMAQ: No

RSTP: Yes

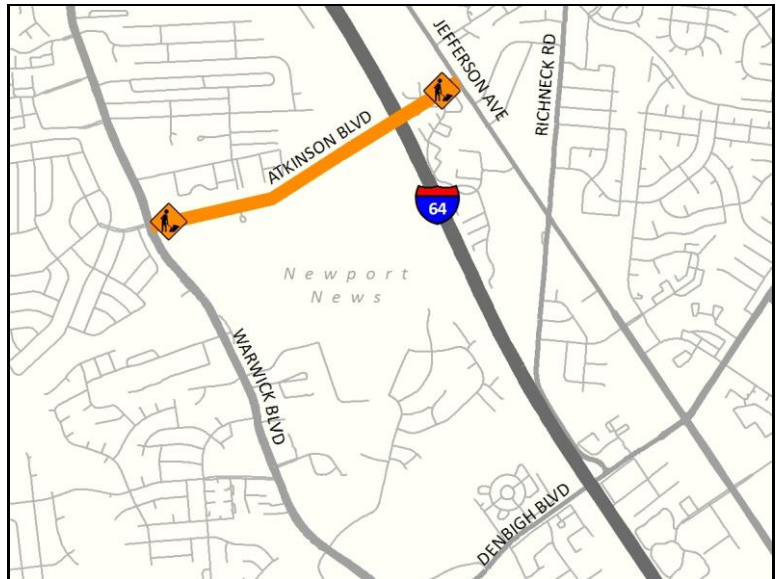

HRTPO Notes

SCHEDULE

	Start	End	Status
Preliminary Engineering	6/8/1987	9/14/2016	Complete
Right of Way	9/14/2016	5/11/2017	Complete
Construction	5/11/2017	9/23/2020	Underway

COSTS AND EXPENDITURES

	Cost Estimates	Total Expenditures	Percent Expended	Recent Expenditures			
				Latest Quarter	Previous 3 Quarters		
				3	2	1	
Preliminary Engineering	\$5,692,574	\$5,692,574	100%	\$0	-	-	-
Right of Way	\$1,891,136	\$694,587	37%	\$0	-	-	-
Construction	\$60,537,493	\$39,304,624	65%	\$0	-	-	-
TOTAL	\$68,121,203	\$45,691,785	67%				

ALLOCATIONS

Fund Source(s)	Previous	FY 2021	FY 2022	FY 2023	FY 2024	TOTAL
STP	\$800,000	\$0	\$0	\$0	\$0	\$800,000
STM	\$9,632,321	\$0	\$0	\$0	\$0	\$9,632,321
STF	\$7,700,726	\$0	\$0	\$0	\$0	\$7,700,726
RSTP	\$40,529,277	\$0	\$0	\$0	\$0	\$40,529,277
RS	\$9,500,000	\$0	\$0	\$0	\$0	\$9,500,000
LOM	\$20,408	\$0	\$0	\$0	\$0	\$20,408
LOC	\$835	\$0	\$0	\$0	\$0	\$835
BOM	\$200,000	\$0	\$0	\$0	\$0	\$200,000
TOTAL	\$68,383,567	\$0	\$0	\$0	\$0	\$68,383,567

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
