

**Denbigh Boulevard Bridge Replacement over I-64
UPC # 93077**

OVERVIEW

Description: Replacement of the bridge on Denbigh Blvd over I-64 and CSX railroad

Street (Route): Denbigh Boulevard (173)

Length (mi): N/A

Jurisdiction/Agency: Newport News

System: Interstate

Scope: Bridge Replacement w/o Added Capacity


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: No

CMAQ: No

RSTP: No

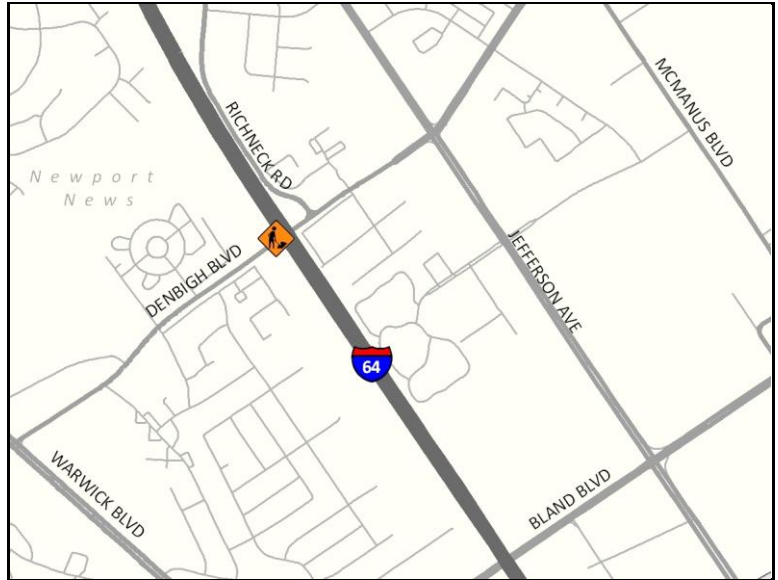

HRTPO Notes

SCHEDULE

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	3/15/2012	10/28/2016	Complete
<i>Right of Way</i>	10/28/2016	9/11/2018	Complete
<i>Construction</i>	9/11/2018	7/27/2021	Underway

COSTS AND EXPENDITURES

Recent Expenditures

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>			
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
				<i>3</i>	<i>2</i>	<i>1</i>	
<i>Preliminary Engineering</i>	\$2,688,000	\$2,672,333	99%	\$0	-	-	-
<i>Right of Way</i>	\$2,509,213	\$806,613	32%	\$0	-	-	-
<i>Construction</i>	\$29,529,369	\$4,799,993	16%	\$0	-	-	-
TOTAL	\$34,726,582	\$8,278,939	24%				

ALLOCATIONS

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>TOTAL</i>
TBD	\$1,240,020	\$0	\$0	\$0	\$0	\$1,240,020
STM	\$268,692	\$0	\$0	\$0	\$0	\$268,692
STF	\$26,791,848	\$0	\$0	\$0	\$0	\$26,791,848
NHS	\$160,000	\$0	\$0	\$0	\$0	\$160,000
NHPP	\$4,266,022	\$0	\$0	\$0	\$0	\$4,266,022
IM	\$2,000,000	\$0	\$0	\$0	\$0	\$2,000,000
TOTAL	\$34,726,582	\$0	\$0	\$0	\$0	\$34,726,582

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
