

**Intelligent Transportation System Improvements  
UPC # 105404**

**OVERVIEW**

**Description:** ITS improvements between Newport News City line and New Kent County line

**Street (Route):** N/A

**Length (mi):** N/A

**Jurisdiction/Agency:** Hampton Roads

**System:** Primary

**Scope:** Safety


**Oversight:** Federal Oversight

**Administered By:** VDOT

**Regionally Significant for Air Quality:** No

**CMAQ:** No

**RSTP:** No

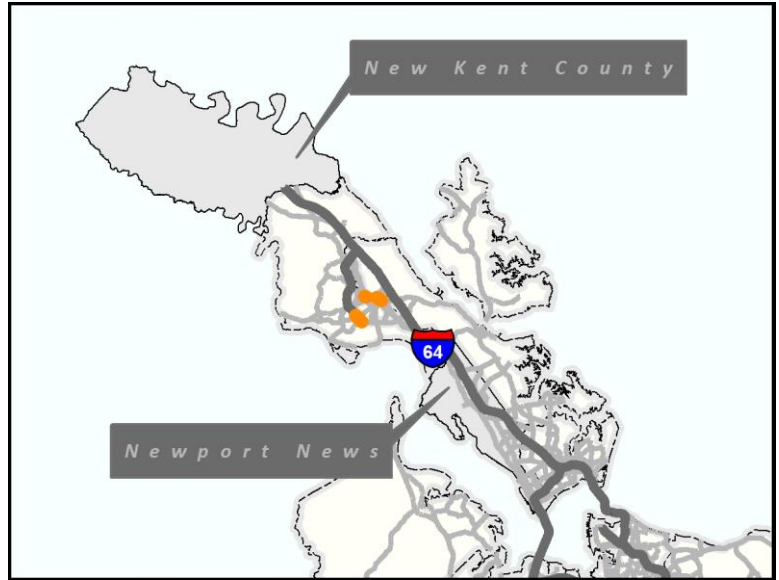

**HRTPO Notes**

**SCHEDULE**

	<i>Start</i>	<i>End</i>	<i>Status</i>
<i>Preliminary Engineering</i>	8/18/2014	1/2/2019	Complete
<i>Right of Way</i>	N/A	N/A	N/A
<i>Construction</i>	N/A	N/A	N/A

**COSTS AND EXPENDITURES**

**Recent Expenditures**

	<i>Cost Estimates</i>	<i>Total Expenditures</i>	<i>Percent Expended</i>	<i>Recent Expenditures</i>			
				<i>Latest Quarter</i>	<i>Previous 3 Quarters</i>		
				<i>3</i>	<i>2</i>	<i>1</i>	
<i>Preliminary Engineering</i>	\$385,000	\$277,435	72%	\$0	-	-	-
<i>Right of Way</i>	\$0	\$0	-	\$0	-	-	-
<i>Construction</i>	\$0	\$0	-	\$0	-	-	-
<b>TOTAL</b>	<b>\$385,000</b>	<b>\$277,435</b>	<b>72%</b>				

**ALLOCATIONS**

<i>Fund Source(s)</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>TOTAL</i>
STF	\$385,000	\$0	\$0	\$0	\$0	\$385,000
<b>TOTAL</b>	<b>\$385,000</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$0</b>	<b>\$385,000</b>

**SCHEDULED OBLIGATIONS**

<i>Phase</i>	<i>Fund Source</i>	<i>Previous</i>	<i>FY 2021</i>	<i>FY 2022</i>	<i>FY 2023</i>	<i>FY 2024</i>	<i>Match</i>
PE	AC		\$385,000				
	<b>Subtotal</b>		<b>\$385,000</b>				
	<b>TOTAL</b>		<b>\$385,000</b>				

Source of Project Data: Virginia Department of Transportation.
