

George Washington Memorial Highway Signal Timing Improvements

UPC # 98806

OVERVIEW

Description: Signal coordination along George Washington Memorial Hwy from the Coleman Bridge to the Route 17/Route 17 Bus intersection

Street (Route): George Washington Memorial Highway (17)

Length (mi): 11.3

Jurisdiction/Agency: Gloucester County

System: Primary

Scope: Safety/Traffic Ops/TSM


Oversight: Federal Oversight

Administered By: VDOT

Regionally Significant for Air Quality: No

CMAQ: Yes

RSTP: No

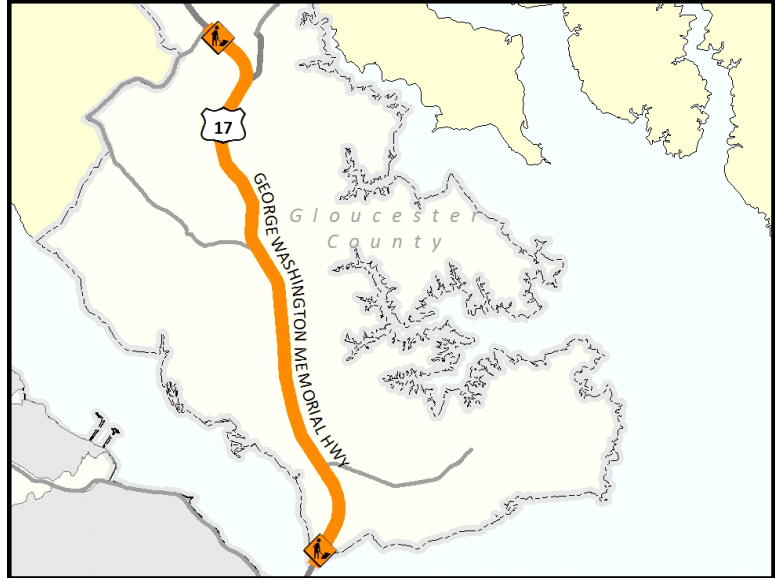

HRTPO Notes

SCHEDULE

	Start	End	Status
Preliminary Engineering	7/18/2012	2/11/2015	Complete
Right of Way	2/11/2015	10/25/2016	Complete
Construction	10/25/2016	12/31/2019	Complete

COSTS AND EXPENDITURES

Recent Expenditures

	Cost Estimates	Total Expenditures	Percent Expended	Latest Quarter	Previous 3 Quarters		
					3	2	1
Preliminary Engineering	\$570,568	\$570,696	100%	\$0	-	-	-
Right of Way	\$90,146	\$90,146	100%	\$0	-	-	-
Construction	\$2,140,281	\$1,771,324	83%	\$0	-	-	-
TOTAL	\$2,800,995	\$2,432,166	87%				

ALLOCATIONS

Fund Source(s)	Previous	FY 2021	FY 2022	FY 2023	FY 2024	TOTAL
STM	\$384,374	\$0	\$0	\$0	\$0	\$384,374
CMAQ	\$2,416,621	\$0	\$0	\$0	\$0	\$2,416,621
TOTAL	\$2,800,995	\$0	\$0	\$0	\$0	\$2,800,995

SCHEDULED OBLIGATIONS

Source of Project Data: Virginia Department of Transportation.
